

Summary Of Major Construction Activities

The work of the early site enabling package began in July of 2018 as part of Phase I of construction. The landscaped area at the front bus loop was cleared, the knoll was cutdown to match adjacent grade, and the new parking area was paved and striped. The existing entrance was widened and divided to provide separate school and construction access driveways. The construction fencing was extended around the existing school to provide separation along the entire the perimeter of the existing school. In addition, construction fencing and erosion controls were installed at the limit of work line. Once the construction site was secured, work on the access road retaining wall began. Excavated soils were exported to the City of Worcester's Clarendon site and the north slope of the site was cleared of trees and brush. A ramp was constructed to provide an alternate path from the lower level to the front of the school.

By the end of October, the retaining wall was completed with loam, low mow seed, plantings, and fencing was installed.

The 60% Construction Documents & Early Site Enabling Package #2 were issued on August 30th and the full Site Package was issued for bid. Phase II of construction began in late October with Ernest Guigli & Sons was awarded the sitework contract. Guigli mobilized on site at the end of October and began work on the existing outfall under the supervision of the Conservation Committee. Work started on the precut for the Support of Excavation (SOE) and the retaining wall along the conservation area. Soil was exported began to the Fish Road Reclamation Site in Dudley, MA. Guigli has also begun the excavation and backfill of material in the classroom sections of the building.

Looking Ahead

- Pre-cut for support of excavation system (SOE)
- Mass excavation and hauling of site of excavated material to disposal facility
- Retaining wall construction at the ring road
- Installation of the SOE system
- Excavation and backfill for the future building
- Installation of utilities (drainage/water/sewer)

Progress Photos




1. Construction of Enabling Package Retaining Wall



2. Parking Lot At Main Entrance



3. Ramp for Access Around School

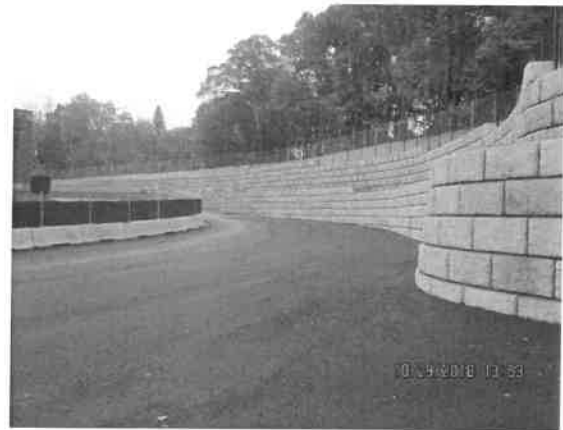

4. Completed Enabling Package Retaining Wall



5. Completed Work at Outfall
